CIVIL QUALITY CONSULTANTS A
PROJECT PLANNING/SCH

Clients Name	:	**Sri.B B Umesha**	
Project Name	:	**IMPROVEMENTS TO ROADS AND DRAINS PROVIDING AMMENITIES CONSTRUCTION OF R DIVISION AS PER ANNEXURE GO NO UDD 217 SFC 2016 DATED 28 5 2016 WORKS SL NO FOR**	
Project Manager /Team Leader	:	**Madhu P**	
Project Start Date	:	**6-Jan-18**	
Project End Date	:	**30-May-18**	
Project Length in Days	:	**144**	**Days**

Sl. No	*Assignment*	*Unit*	*Boq Qnty*	*Qty of Work*	*Percentage of Work done*	*Status of Work*	*Start Date*	*End Date*	*No. of Working Days*
1	KSRRB M300-1. Earth work excavation by manual means in ordinary soil involving an	Cum	3386.10	3386.10	100.00	Completed	7-Jan-18	22/Jan/18	15
2	KSRB 2-1.1 : Earthwork in surface excavation in ordinary soil for levelling and lowering the	Cum	945.00	945.00	100.00	Completed	12/Jan/18	28/Jan/18	16
3	Removing & Refixing Stone slabs of drains and Pointing in C.M(1:3) with all lead and lift ,	Sqm	4590.00	4590.00	100.00	Completed	16/Jan/18	29/Jan/18	13
4	Providing granite Slabs of Selected quality roughly dressed and fixed in cement mortor (1:6)	Sqm	540.00	540.00	100.00	Completed	19/Jan/18	2/Feb/18	14
5	KSRRB M200-13.1. Dismantling of existing structures like culverts, Bridges, retaining walls	Cum	129.45	129.45	100.00	Completed	6/Jan/18	20/Jan/18	14
6	KSRB 4-1.2: Providing and laying in position plain cement concrete of mix 1:3:6 with OPC	Cum	149.44	149.44	100.00	Completed	18/Jan/18	31/Jan/18	13
7	KSRB 5.2-3 : Providing and constructing granite / trap / basalt size stone masonry in foundation with	Cum	84.38	84.38	100.00	Completed	21/Jan/18	4/Feb/18	14
8	KSRB 5.3-3 : Providing and constructing granite / trap / basalt size stone masonry in basement with	Cum	48.80	48.80	100.00	Completed	28/Jan/18	13/Feb/18	16
9	KSRB 15.1.3 Providing ruled pointing to coursed stone masonry with cement mortar 1:3, 20mm	Sqm	216.90	216.90	100.00	Completed	5/Feb/18	16/Feb/18	11
10	KSRB 4-1.6 ; Providing and laying in position plain cement concrete of mix 1:2:4 with cement	Cum	10.84	10.84	100.00	Completed	6/Feb/18	18/Feb/18	12
11	Supplying and fixing M.S. Rectangular poles made out of 2 equal angles of 65x65x6 mm	m	277.20	277.20	100.00	Completed	8/Feb/18	20/Feb/18	12
12	Providing chain link fencing 50mm size of 8 guage properly stretched between existing	Sqm	361.50	361.50	100.00	Completed	12/Feb/18	24/Feb/18	12
13	Providing and fixing M.S. Block pipe of 38mm dia, of heavy guage of 14 including removing the	m	482.00	482.00	100.00	Completed	16/Feb/18	28/Feb/18	12
14	KSRRB M300-52.2. Scarifying Existing Bituminous surface to a depth of 50mm by	Sqm	3618.50	3618.50	100.00	Completed	20/Feb/18	6/Mar/18	14
15	KSRRB M300-14. Excavation for roadwork in soil with hydraulic excavator of 0.90 cum bucket	Cum	2092.33	2092.33	100.00	Completed	24/Feb/18	14/Mar/18	18
16	KSRRB M 400-17, Providing, laying, spreading and compacting graded stone aggregate to wet	Cum	2881.66	2881.66	100.00	Completed	2/Mar/18	17/Mar/18	15
17	KSRRB M 500-6, Providing and applying primer coat with SS bitumen emulsion on prepared	Sqm	11862.00	11862.00	100.00	Completed	7/Mar/18	22/Mar/18	15
18	KSRRB 500-2: Cleaning the existing black topped surface with brooms, soft brushes and	Sqm	44061.50	44061.50	100.00	Completed	10/Mar/18	14/Mar/18	4
19	KSRRB M500-7 : Providing and applying tack coat using 80/100 grade bitumen (VG10) on	Sqm	55923.50	55923.50	100.00	Completed	12/Mar/18	22/Mar/18	10
20	KSRRB M500-19. Providing and laying bituminous concrete 30-40 mm compacted	Cum	2227.28	2227.28	100.00	Completed	19/Mar/18	3/Apr/18	15

NGINEERS
LE

TER PLANT BANGALURU ONE CENTER PROVIDING SODIUM VAPOUR LIGHTS SIGN BOARDS IN WARD NO 9 10 AND 11 BYATARAYANAPURA
D NO 9 33 To 34 WARD NO 10 35 TO 38 WARD NO 11 39 TO 48.

Delay Reason : Site Clearness

Jan-18	Feb-18	Mar-18	Apr-18	May-18

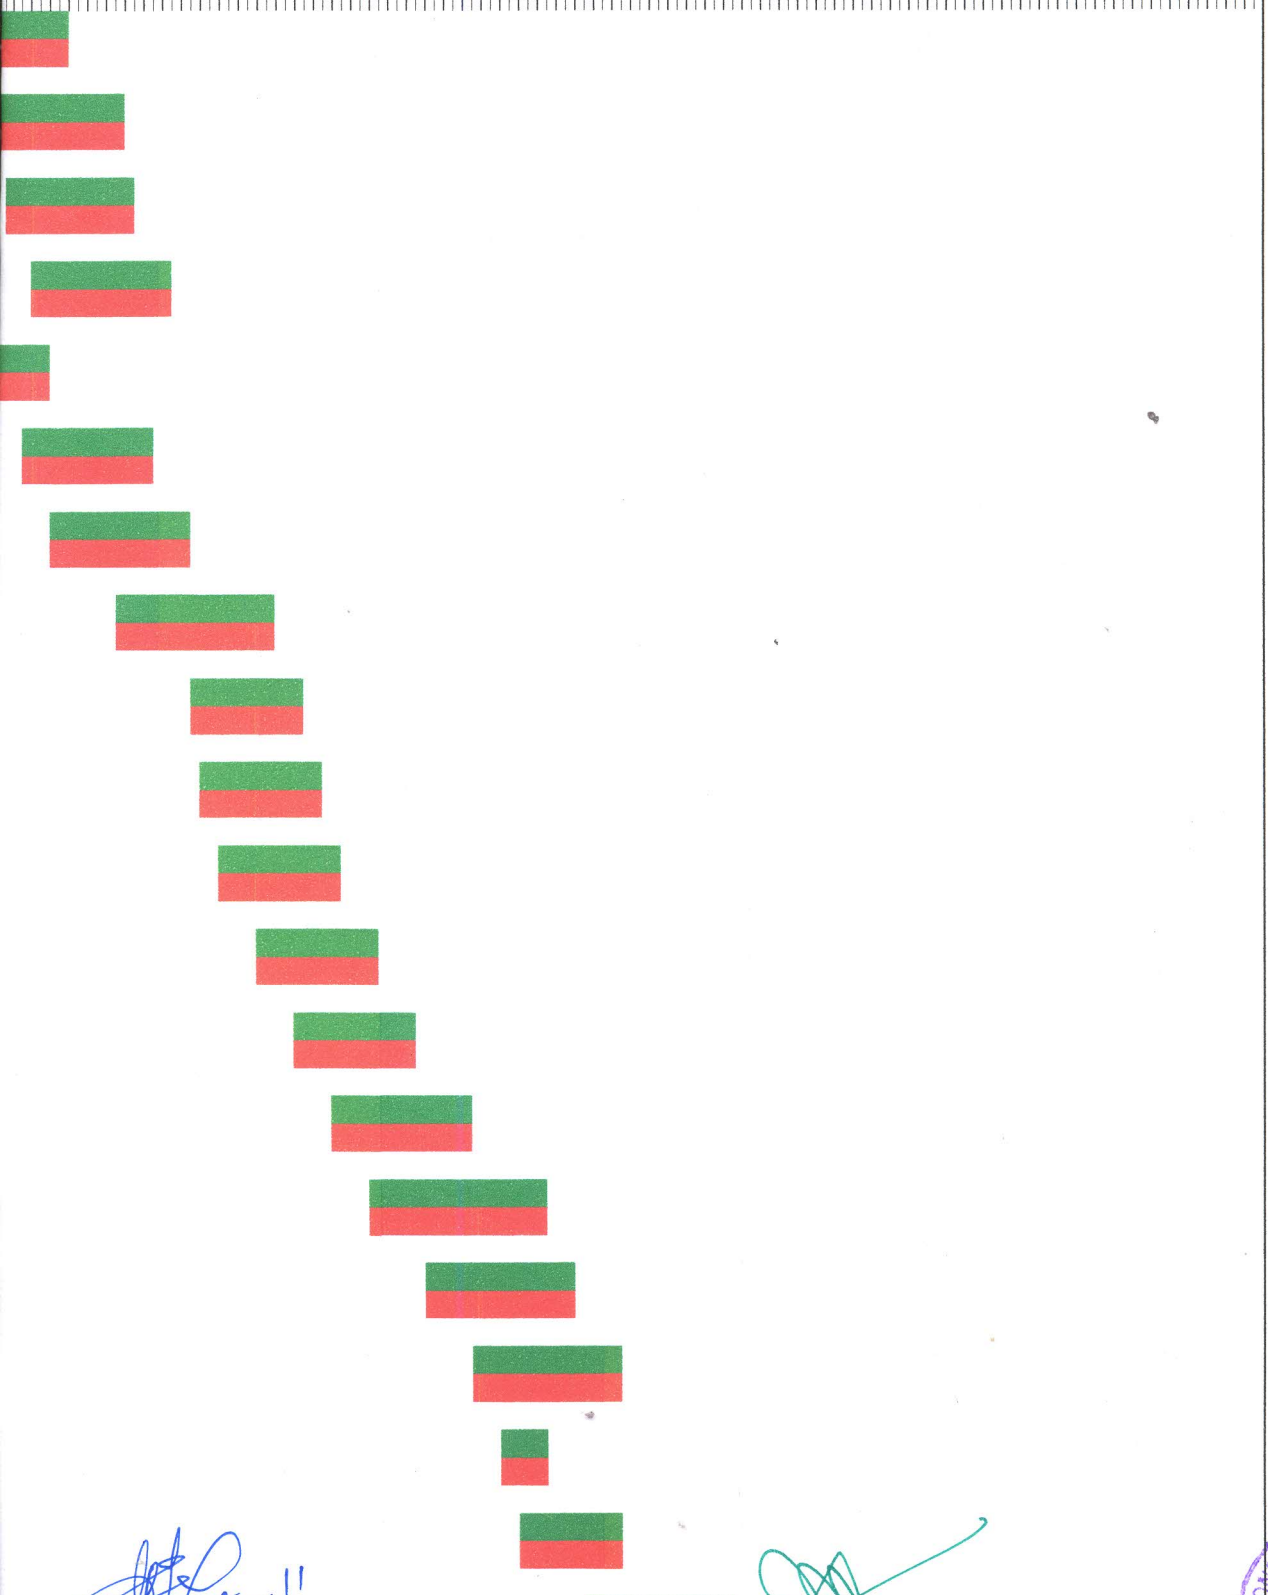

Assistant Executive Engineer
Vidyaranyapura Sub Division
BBMP, Bangalore - 97

21	Cement concrete pavement.Construction of un-reinforced plain cement concrete pavement,	Cum	115.80	115.80	100.00	Completed	29/Mar/18	14/Apr/18	16
22	Vaccum de-watering with vaccum pump and suction mat and compaction with skin floater	Sqm	1158.00	1158.00	100.00	Completed	4/Apr/18	30/Apr/18	26
23	Providing and fixing Pre cast solid concrete kerb stones made out of CC 1:2:4 with top and bottom	No.	644.00	644.00	100.00	Completed	1/Apr/18	18/Apr/18	17
24	KSRRB 800-1. Painting two coats after filling the surface with synthetic enamel paint in approved	Sqm	101.50	101.50	100.00	Completed	13/Apr/18	25/Apr/18	12
25	KSRRB M400-19: Construction of Median and island above road level with approved material	Cum	58.00	58.00	100.00	Completed	20/Apr/18	2/May/18	12
26	KSRB 14.6-1: Providing and laying heavy duty cobble stones 60mm thick interlock pavers, using	Sqm	290.00	290.00	100.00	Completed	27/Apr/18	13/May/18	16
27	Providing and fixing M.S. Gate as per Chief Architect Drawing, using 50mm x 50mm 14	Sqm	22.50	22.50	100.00	Completed	8/May/18	9/May/18	1
28	KSRRB M800-13. Providing and laying of hot applied thermoplastic compound 2.5 mm thick	Sqm	544.25	544.25	100.00	Completed	24/Mar/18	9/Apr/18	16
29	Geophysical investigation of site for sinking Borewell for supplying drinking water to the	Each BW	6.00	6.00	100.00	Completed	29/Apr/18	30/Apr/18	1
30	Sinking borewell of 165 mm dia clear using super fast hydraulic rig of capacity 250 PSIG & above	Rmtr	300.00	300.00	100.00	Completed	2/May/18	4/May/18	2
31	Sinking borewell of 165 mm dia clear using super fast hydraulic rig of capacity 250 PSIG & above	Rmtr	300.00	300.00	100.00	Completed	2/May/18	4/May/18	2
32	Sinking borewell of 165 mm dia clear using super fast hydraulic rig of capacity 250 PSIG & above	Rmtr	300.00	300.00	100.00	Completed	2/May/18	4/May/18	2
33	Sinking borewell of 165 mm dia clear using super fast hydraulic rig of capacity 250 PSIG & above	Rmtr	300.00	300.00	100.00	Completed	2/May/18	4/May/18	2
34	Sinking borewell of 165 mm dia clear using super fast hydraulic rig of capacity 250 PSIG & above	Rmtr	300.00	300.00	100.00	Completed	2/May/18	4/May/18	2
35	Supply of ISI mark 175 mm nominal bore, Plain end steel casing pipe - grade of Steel Fee 410 of	Rmtr	300.00	300.00	100.00	Completed	2/May/18	4/May/18	2
36	Providing 250mm dia PVC Pipe 6kg/cm SE PRED Approved Rate with all lead and lift ,	Rmtr	108.00	108.00	100.00	Completed	4/May/18	12/May/18	8
37	Providing and fixing 160mm Borewell Cap P. iii, with all lead and lift , loading and unloading and	Rmtr	6.00	6.00	100.00	Completed	4/May/18	5/May/18	1
38	Supply and delivery at site brand New texmo/ innoval/ Lubi/ Sabar / Atalanta/ Calamal/ make	No	6.00	6.00	100.00	Completed	5/May/18	8/May/18	3
39	Supplying of ISI marked galvanized mild steel tube (continously welded electric resistance	Rmtr	1500.00	1500.00	100.00	Completed	8/May/18	11/May/18	3
40	Heavy Duty Collar 50 mm dia with all lead and lift , loading and unloading and allother incidental	No	264.00	264.00	100.00	Completed	8/May/18	11/May/18	3
41	Supplying and drawing 3 core flat PVC sheathed submersible pump cable manufactured with	Mtr	3060.00	3060.00	100.00	Completed	8/May/18	11/May/18	3
42	Erection of pumpset including aligning and balancing with all necessary erection materials	Nos	6.00	6.00	100.00	Completed	8/May/18	11/May/18	3
43	Supplying and fixing 20"x20"x2.5" polished wood board made of not less than 15mm thick	Each	6.00	6.00	100.00	Completed	8/May/18	11/May/18	3
44	Supplying of 1.1 KV LT UG cable having aluminum conductor PVC insulated, extruded	Mtr	180.00	180.00	100.00	Completed	8/May/18	11/May/18	3
45	Labour charges for laying of 1.1 KV class UG cable in existing trench GI pipe / stoneware pipe /	Mtr	180.00	180.00	100.00	Completed	8/May/18	11/May/18	3

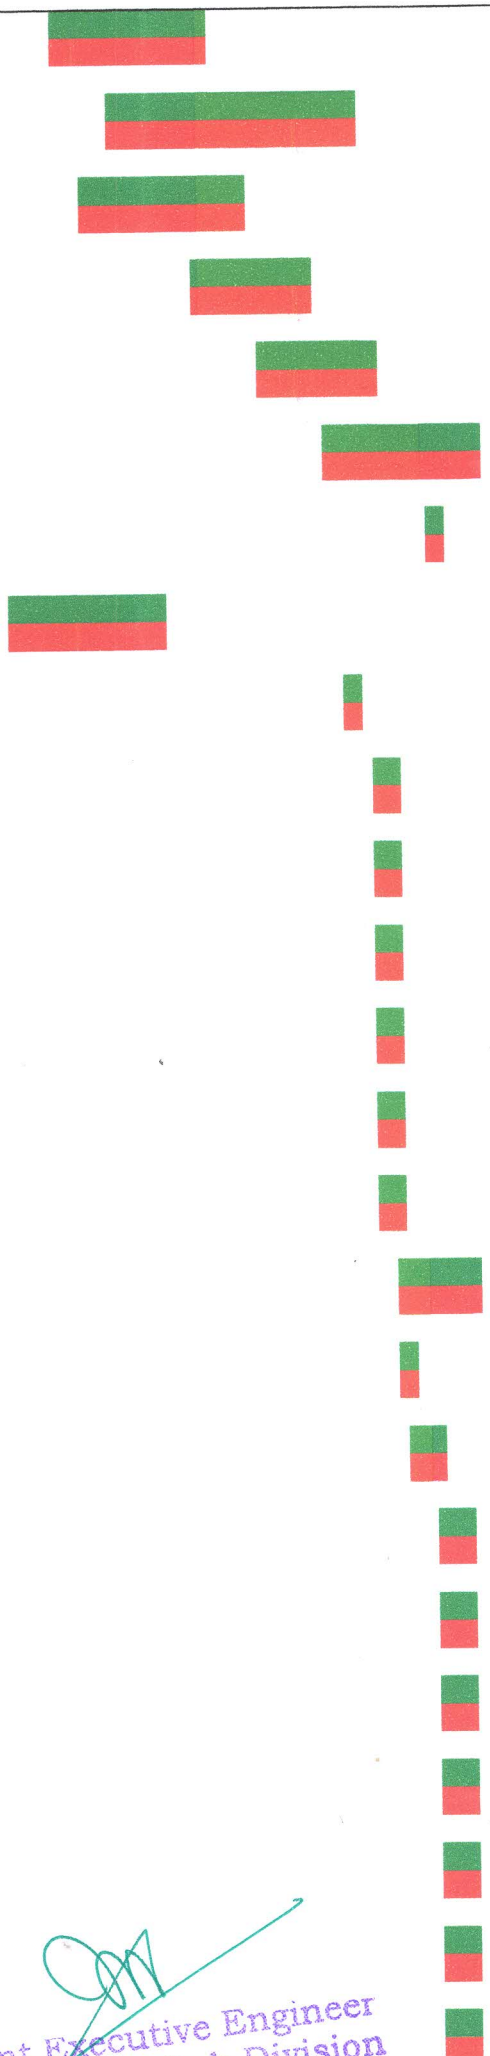

Assistant Executive Engineer
Vidyaranyapura Sub Division
BBMP, Bangalore - 97

CIVIL CONSULTANTS & ENGINEERS
Bangalore

46	Digging of trench of 0.6m deep x 0.50 mtr wide refilling the trench to the required ground level	Mtr	150.00	150.00	100.00	Completed	11/May/18	21/May/18	10
47	Supplying and fixing of class A (medium duty) GI pipe of wall thickness not less than 3.25mm on	Mtr	24.00	24.00	100.00	Completed	15/May/18	23/May/18	8
48	Supplying and fixing L.T. cast Iron pot heads suitable for 1.1 KV class UG cable filled with	No	6.00	6.00	100.00	Completed	16/May/18	19/May/18	3
49	Supplying, fixing, wiring, earth electrode for grounding conduits, I.C. cutouts and other	No	6.00	6.00	100.00	Completed	19/May/18	21/May/18	2
50	Supplying & fixing of Porcelain fuse channel with cut out on existing wooden/panel using necessary	No	36.00	36.00	100.00	Completed	19/May/18	21/May/18	2
51	KSRB 13-7.1-4: Providing and fixing in position 50mm nominal bore gun metal non-return valve	No	6.00	6.00	100.00	Completed	19/May/18	21/May/18	2
52	Providing NP/CP waste unions conforming to ISI specifications and fixing them in position as per	No	6.00	6.00	100.00	Completed	19/May/18	21/May/18	2
53	Supplying and fixing 50mm dia GI X nipple with ISI mark with all lead and lift loading unloading	No	24.00	24.00	100.00	Completed	19/May/18	21/May/18	2
54	Supplying shunt capaitors conforming to IS 2834, 3phase 400/440 volts grade for power factor	No	6.00	6.00	100.00	Completed	19/May/18	21/May/18	2
55	Supplying and fixing miniature circuit breakers on existing MCB distribution boards using necessary	No	6.00	6.00	100.00	Completed	19/May/18	21/May/18	2
56	Fabricating supplying and mounting MS box made out ... SWG suitable for floor / wall	No	131400.00	131400.00	100.00	Completed	19/May/18	21/May/18	2
57	Supplying and delivery at site brand new star / Essen/ Lotus/Sun-shines/Adarsh/ GK Controls	No	6.00	6.00	100.00	Completed	19/May/18	21/May/18	2
58	Earthwork excavation for pipeline trenches including deporiting or bank up to a lead of 50	Cum	162.00	162.00	100.00	Completed	19/May/18	25/May/18	6
59	Providing and instalation at site of works P.V.C.Pipes including cost of pipes and specials	Rmtr	360.00	360.00	100.00	Completed	18/May/18	24/May/18	6
60	Refilling the basement and pipeline treanches with secleted available earthe for trench	Cum	162.00	162.00	100.00	Completed	15/May/18	21/May/18	6
61	KSRB 13.6.3-6 : Providing and fixing in position brass gate valve with C.I wheel of approved	Each	12.00	12.00	100.00	Completed	19-May-18	22/May/18	3
62	KSRB 2-2.2 : Earth work excavation for foundation of buildings, culverts water supply,	Cum	213.12	213.12	100.00	Completed	18/Mar/18	4/Apr/18	17
63	KSRB 2.14-1: Extra for additional lift of 1.5m. or part thereof for excavation In loose / soft or hard	Cum	27.04	27.04	100.00	Completed	25/Mar/18	9/Apr/18	15
64	Providing and laying in position plain cement concrete of mix 1:3:6 with OPC cement	Cum	8.49	8.49	100.00	Completed	30/Mar/18	9/Apr/18	10
65	KSRB 4-1.3 : Providing and laying in position plain cement concrete of mix 1:4:8 with OPC	Cum	40.33	40.33	100.00	Completed	4/Apr/18	16/Apr/18	12
66	KSRB 5.2.3 : Providing and constructing granite / trap / basalt size stone masonry in foundation with	Cum	33.48	33.48	100.00	Completed	26/Apr/18	11/May/18	15
67	KSRB 5.3-3 : Providing and constructing granite / trap / basalt size stone masonry in basement with	Cum	15.04	15.04	100.00	Completed	11/Apr/18	1/May/18	20
68	KSRB 2.3 : Filling available excavated earth (excluding rock) in sides of foundations upto	Cum	237.58	237.58	100.00	Completed	26/Apr/18	1/May/18	5
69	KSRB 5-11 : Providing and constructing load bearing wall with solid concrete blocks of size	Sqm	603.98	603.98	100.00	Completed	29/Apr/18	11/May/18	12
70	KSRB 4.2.2 : Providing and laying in position reinforced cement concrete of design mix M20	Cum	77.10	77.10	100.00	Completed	26/Apr/18	8/May/18	12

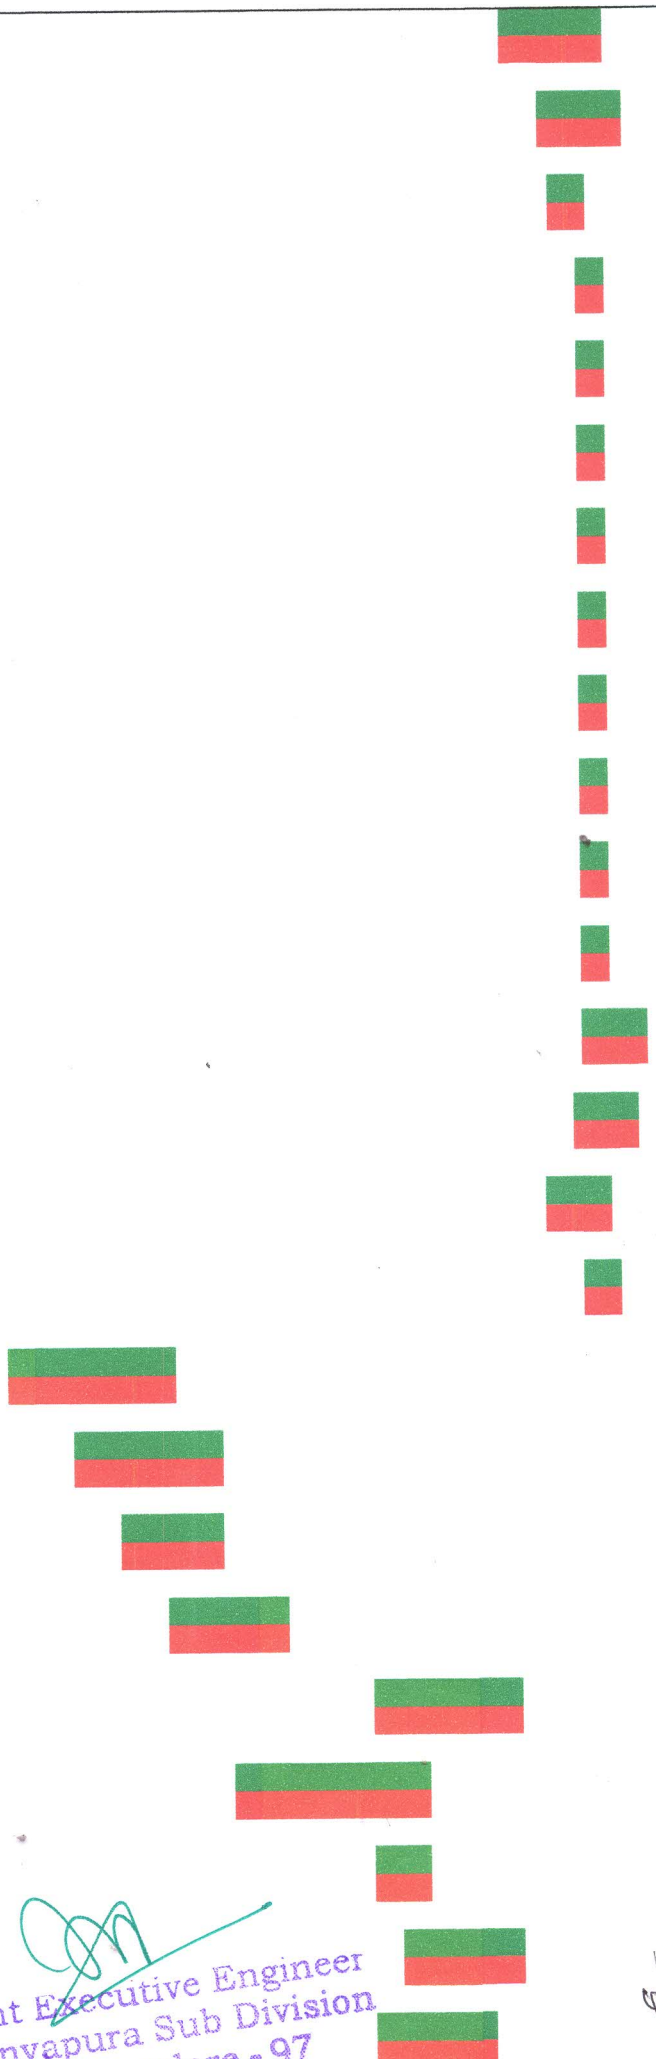

Assistant Executive Engineer
Vidyaranyapura Sub Division
BBMP, Bangalore - 97

QUALITY CONSULTANTS & ENGINEERS
Bangalore

71	KSRB 4.2.8: Providing and laying in position reinforced cement concrete of design mix M20	Cum	31.16	31.16	100.00	Completed	28/Apr/18	10/May/18	12
72	KSRB 4.2.10 : Providing and laying in position reinforced cement concrete ofmix M20 with OPC	Sqm	42.38	42.38	100.00	Completed	2/May/18	14/May/18	12
73	KSRB 4.9.1: Providing TMT steel reinforcement for R.C.C work including straightening, cutting,	MT	12.85	12.85	100.00	Completed	23/Apr/18	6/May/18	13
74	KSRB 4-6.1 : Providing and removing centering, shuttering, strutting, propping etc., and removal of	Sqm	51.84	51.84	100.00	Completed	19/Apr/18	29/Apr/18	10
75	KSRB 4-6.4 : Providing and removing centering, shuttering, strutting, propping etc., and removal of	Sqm	400.54	400.54	100.00	Completed	27/Apr/18	7/May/18	10
76	KSRB 4-6.5 : Providing and removing centering, shuttering, strutting, propping etc., for columns,	Sqm	129.36	129.36	100.00	Completed	29/Apr/18	8/May/18	9
77	KSRB 4-6.2 : Providing and removing centering, shuttering, strutting, propping etc., and removal of	Sqm	142.84	142.84	100.00	Completed	6/May/18	18/May/18	12
78	KSRB 4-6.7 :Providing and removing centering, shuttering, strutting, propping etc., and removal of	Sqm	120.69	120.69	100.00	Completed	10/May/18	18/May/18	8
79	KSRB 4-6.10 : Providing and removing centering, shuttering, strutting, propping etc., for chajjas,	Sqm	46.44	46.44	100.00	Completed	10/May/18	18/May/18	8
80	KSRB 15.3.13 : Providing 12mm thick cement plaster in single coat with cement mortar 1:3, to	Sqm	241.84	241.84	100.00	Completed	4/May/18	14/May/18	10
81	KSRB 15.3.11 :Providing 20mm thick cement plaster in single coat with cement mortar 1:4, to	Sqm	264.72	264.72	100.00	Completed	5/May/18	15/May/18	10
82	KSRB15-3.10 : Providing 20mm thick cement plaster in single coat with cement mortar 1:6, to	Sqm	280.40	280.40	100.00	Completed	6/May/18	16/May/18	10
83	KSRB 15.3.2 Providing 12mm thick cement plaster in single coat with cement mortar 1:4, to	Sqm	225.90	225.90	100.00	Completed	7/May/18	17/May/18	10
84	KSRB 15.10.2 Providing white washing for every one additional coat with lime of approved quality,	Sqm	225.90	225.90	100.00	Completed	8/May/18	18/May/18	10
85	KSRB 15.10.4 Providing white washing to ceiling and / or sloping roof surface with additional one	Sqm	126.22	126.22	100.00	Completed	9/May/18	19/May/18	10
86	KSRB 15-7 : Providing lime rendering for plastering to wall and ceiling, including cost of	Sqm	380.34	380.34	100.00	Completed	10/May/18	20/May/18	10
87	KSRB 15.3.9: Providing 18mm thick cement plaster in single coat with cement mortar 1:6, to	Sqm	345.36	345.36	100.00	Completed	11/May/18	21/May/18	10
88	KSRB 15-14.1 : Providing and applying two coats with oil bound washable distemper of approved	Sqm	645.06	645.06	100.00	Completed	12/May/18	22/May/18	10
89	KSRB 15-16.1: providing and finishing external walls in tow coats with water proof cement paint	Sqm	625.75	625.75	100.00	Completed	13/May/18	23/May/18	10
90	Providing and applying two coats with Plastic emulsion paint of approved brand wall surface to	Sqm	225.90	225.90	100.00	Completed	14/May/18	24/May/18	10
91	Providing and applying two coats with Plastic emulsion paint of approved brand wall surface to	Sqm	126.22	126.22	100.00	Completed	15/May/18	25/May/18	10
92	Providing vitrified tiles 60 x 60cms of approved make, shade and size for flooring laid on a bed of	Sqm	75.00	75.00	100.00	Completed	9/May/18	17/May/18	8
93	KSRB 14-17.2 : Providing skirting, dado, rises of steps with colour glazed tiles on 10mm thick	Sqm	7.53	7.53	100.00	Completed	11/May/18	21/May/18	10
94	KSRB 9.4-2 : Providing Honne wood frames of doors, windows, clerestory windows, ventilators	Cum	0.34	0.34	100.00	Completed	19/May/18	21/May/18	2
95	KSRB 9.5-2 : Providing and fixing in position fully panelled Honne wood shutters for doors,	Sqm	9.45	9.45	100.00	Completed	19/May/18	20/May/18	1

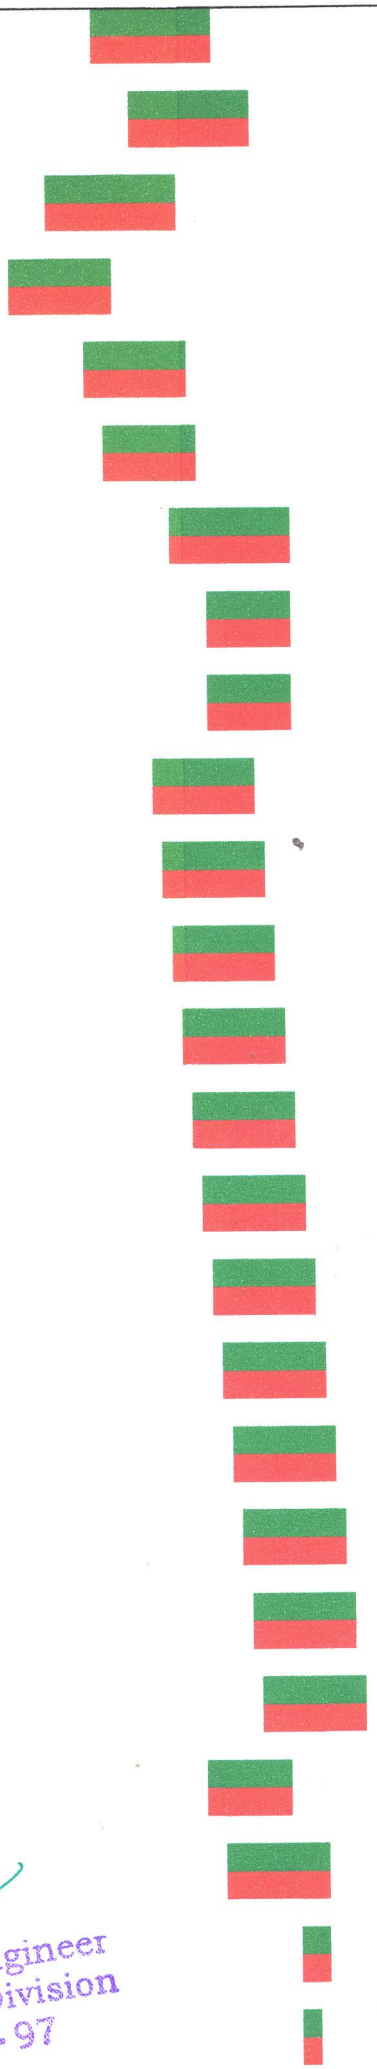

Assistant Executive Engineer
Vidyaranyapura Sub Division
BBMP, Bangalore - 97

CIVIL QUALITY CONSULTANTS & ENGINEERS
Bangalore

96	KSRB 7.9:Providing and fixing .S.gill work for windows and ventilators using M.S.flats, or M.S.	Kgs	725.76	725.76	100.00	Completed	20/May/18	23/May/18	3
97	KSRB 7.10 : Providing and fixing in position aluminium windows and ventilators as per	Sqm	34.56	34.56	100.00	Completed	19/May/18	22/May/18	3
98	KSRB 15-17.4 : Applying priming coat over new wood surface and / or wood based surface, after	Sqm	9.45	9.45	100.00	Completed	21/May/18	24/May/18	3
99	Providing and applying painting two coats (excluding priming coat) on new wood surface	Sqm	9.45	9.45	100.00	Completed	21/May/18	24/May/18	3
100	KSRB 15-18.2 : Providing and applying enamel metal paint two coats (excluding priming coat)	Sqm	210.32	210.32	100.00	Completed	21/May/18	24/May/18	3
101	Providing and fixing Special make glazed Vitrified tiles (Granomite finis) of approved	Sqm	246.58	246.58	100.00	Completed	21/May/18	24/May/18	3
102	Providing and laying/fixing cement base, precast pre polished cement concrete, designer tiles	Sqm	27.00	27.00	100.00	Completed	21/May/18	24/May/18	3
103	KSRB 7.7 : Providing and fixing in position in cement concrete 1:3:6 steel glazed windows and	Sqm	6.48	6.48	100.00	Completed	21/May/18	24/May/18	3
104	KSRB: 7.5 Providing and fixing pull and push type rolling shutters of approved make out of 18	Sqm	45.00	45.00	100.00	Completed	21/May/18	24/May/18	3
105	Providing reverse osmosis system to cover 2000 Liters of High TDS water per hour with RAW	Nos	6.00	6.00	100.00	Completed	21/May/18	24/May/18	3
106	Supplying and wiring adopting loop system in existing PVC Conduit / casing capping using	Point	12.00	12.00	100.00	Completed	2/May/18	12/May/18	10
107	Supplying and wiring adopting loop system in existing PVC Conduit / casing capping using	Point	12.00	12.00	100.00	Completed	10/May/18	20/May/18	10
108	Supplying and flush mounting teak wooden box without front plank, made of not less than 12mm	Each	72.00	72.00	100.00	Completed	18/May/18	21/May/18	3
109	Supplying and flush mounting teak wooden box without front plank, made of not less than 12mm	Each	36.00	36.00	100.00	Completed	19/May/18	22/May/18	3
110	Supplying and flush mounting teak wooden box without front plank, made of not less than 12mm	Each	36.00	36.00	100.00	Completed	20/May/18	22/May/18	2
111	Supplying 4mm thick plastic sheet with necessary nitches for fixing switches, regulators etc., and	Sqcm	39999.96	39999.96	100.00	Completed	20/May/18	22/May/18	2
112	Extra for Groove cutting in brick wall/CC floor to the suitable depth for concealing of Conduit/GI	Mtr	60.00	60.00	100.00	Completed	20/May/18	23/May/18	3
113	Supplying heavy gauge PVC Conduit Pipe 19/20 mm dia 2 mm thick with suitable size bends,	Mtr	60.00	60.00	100.00	Completed	17/May/18	22/May/18	5
114	Supplying and fixing PBBC/Bakelite straight or slant batten holder and wiring with 60w/230 volts	Each	12.00	12.00	100.00	Completed	20/May/18	23/May/18	3
115	Supplying patti type fluorescent tube light fitting of 2' - suitable for 14 watts fluorescent tube	Each	24.00	24.00	100.00	Completed	21/May/18	23/May/18	2
116	Wiring for lighting/power circuit using one of FRLS PVC insulated 1100V grade, multistrand	Mtr	30.00	30.00	100.00	Completed	21/May/18	23/May/18	2
117	Supplying and fixing cast Aluminum round or oblong type bulk head fitting with GI wire guard,	Each	24.00	24.00	100.00	Completed	21/May/18	24/May/18	3
118	Supplying, fixing, wiring, earth electrode for grounding conduits, I.C. cutouts and other	No	6.00	6.00	100.00	Completed	22/May/18	27/May/18	5
119	LED Street light.Supply of LED Streetlight with pressure die cast aluminum housing body with	Each	108.00	108.00	100.00	Completed	23/May/18	27/May/18	4
120	Supplying and Fixing of.....mm dia class A GI pipe bracket up to 2 mtrs long bent at suitable	Each	171.00	171.00	100.00	Completed	27/May/18	28/May/18	1

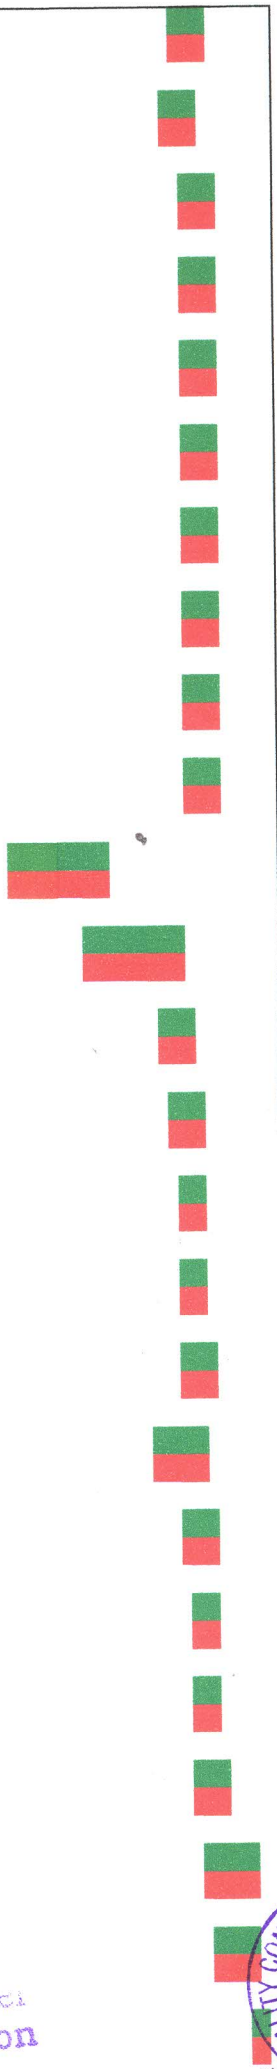

Assistant Executive Engineer
Vidyaranyapura Sub Division
BBMP, Bangalore - 97

QUALITY CONSULTANTS & ENGINEERS
Bangalore

121	Wiring for lighting/power circuit using one of PVC insulated 1100v grade stranded Aluminium	Each	600.00	600.00	100.00	Completed	18/May/18	30/May/18	12
122	Supplying of 1.1 KV LT UG cable having aluminum conductor PVC insulated, extruded	Per Mtr	160.00	160.00	100.00	Completed	28/May/18	29/May/18	1
123	Labour charges for laying of 1.1 KV class UG cable in existing trench GI pipe / stoneware pipe /	Per Mtr	160.00	160.00	100.00	Completed	26/May/18	28/May/18	2
124	Thiristor based single/ Three phase smart street light control and monitoring system Remotely	Each	25.00	25.00	100.00	Completed	23/May/18	27/May/18	4
125	Supplying tinned copper lugs and crimping and wiring to terminal point for wire of the following	Each	66.00	25.00	37.88	Completed	22/May/18	27/May/18	5

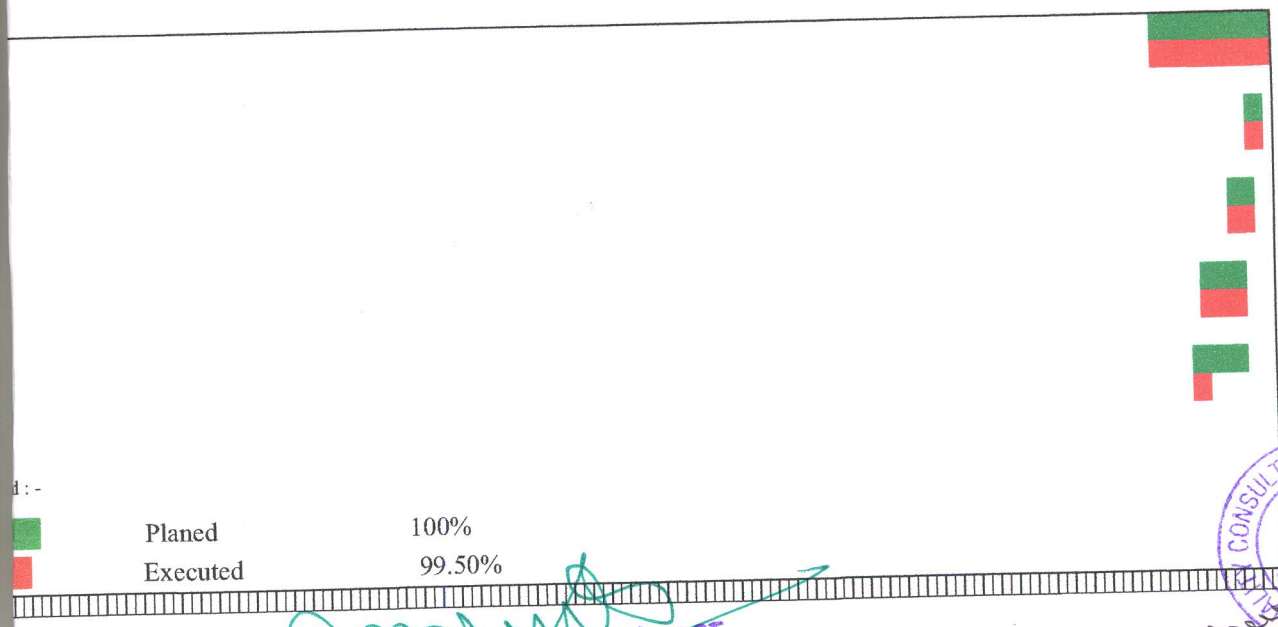

d:-

	Planed	100%
	Executed	99.50%

Assistant Executive Engineer
Vidyaranyapura Sub Division
BBMP, Bangalore - 97

CIVIL CONSULTANTS & ENGINEERS Bangalore
